


Hurd-Wyman Elementary School | Woburn

Neighborhood Meeting - March 01, 2017

Proposed Site Plan

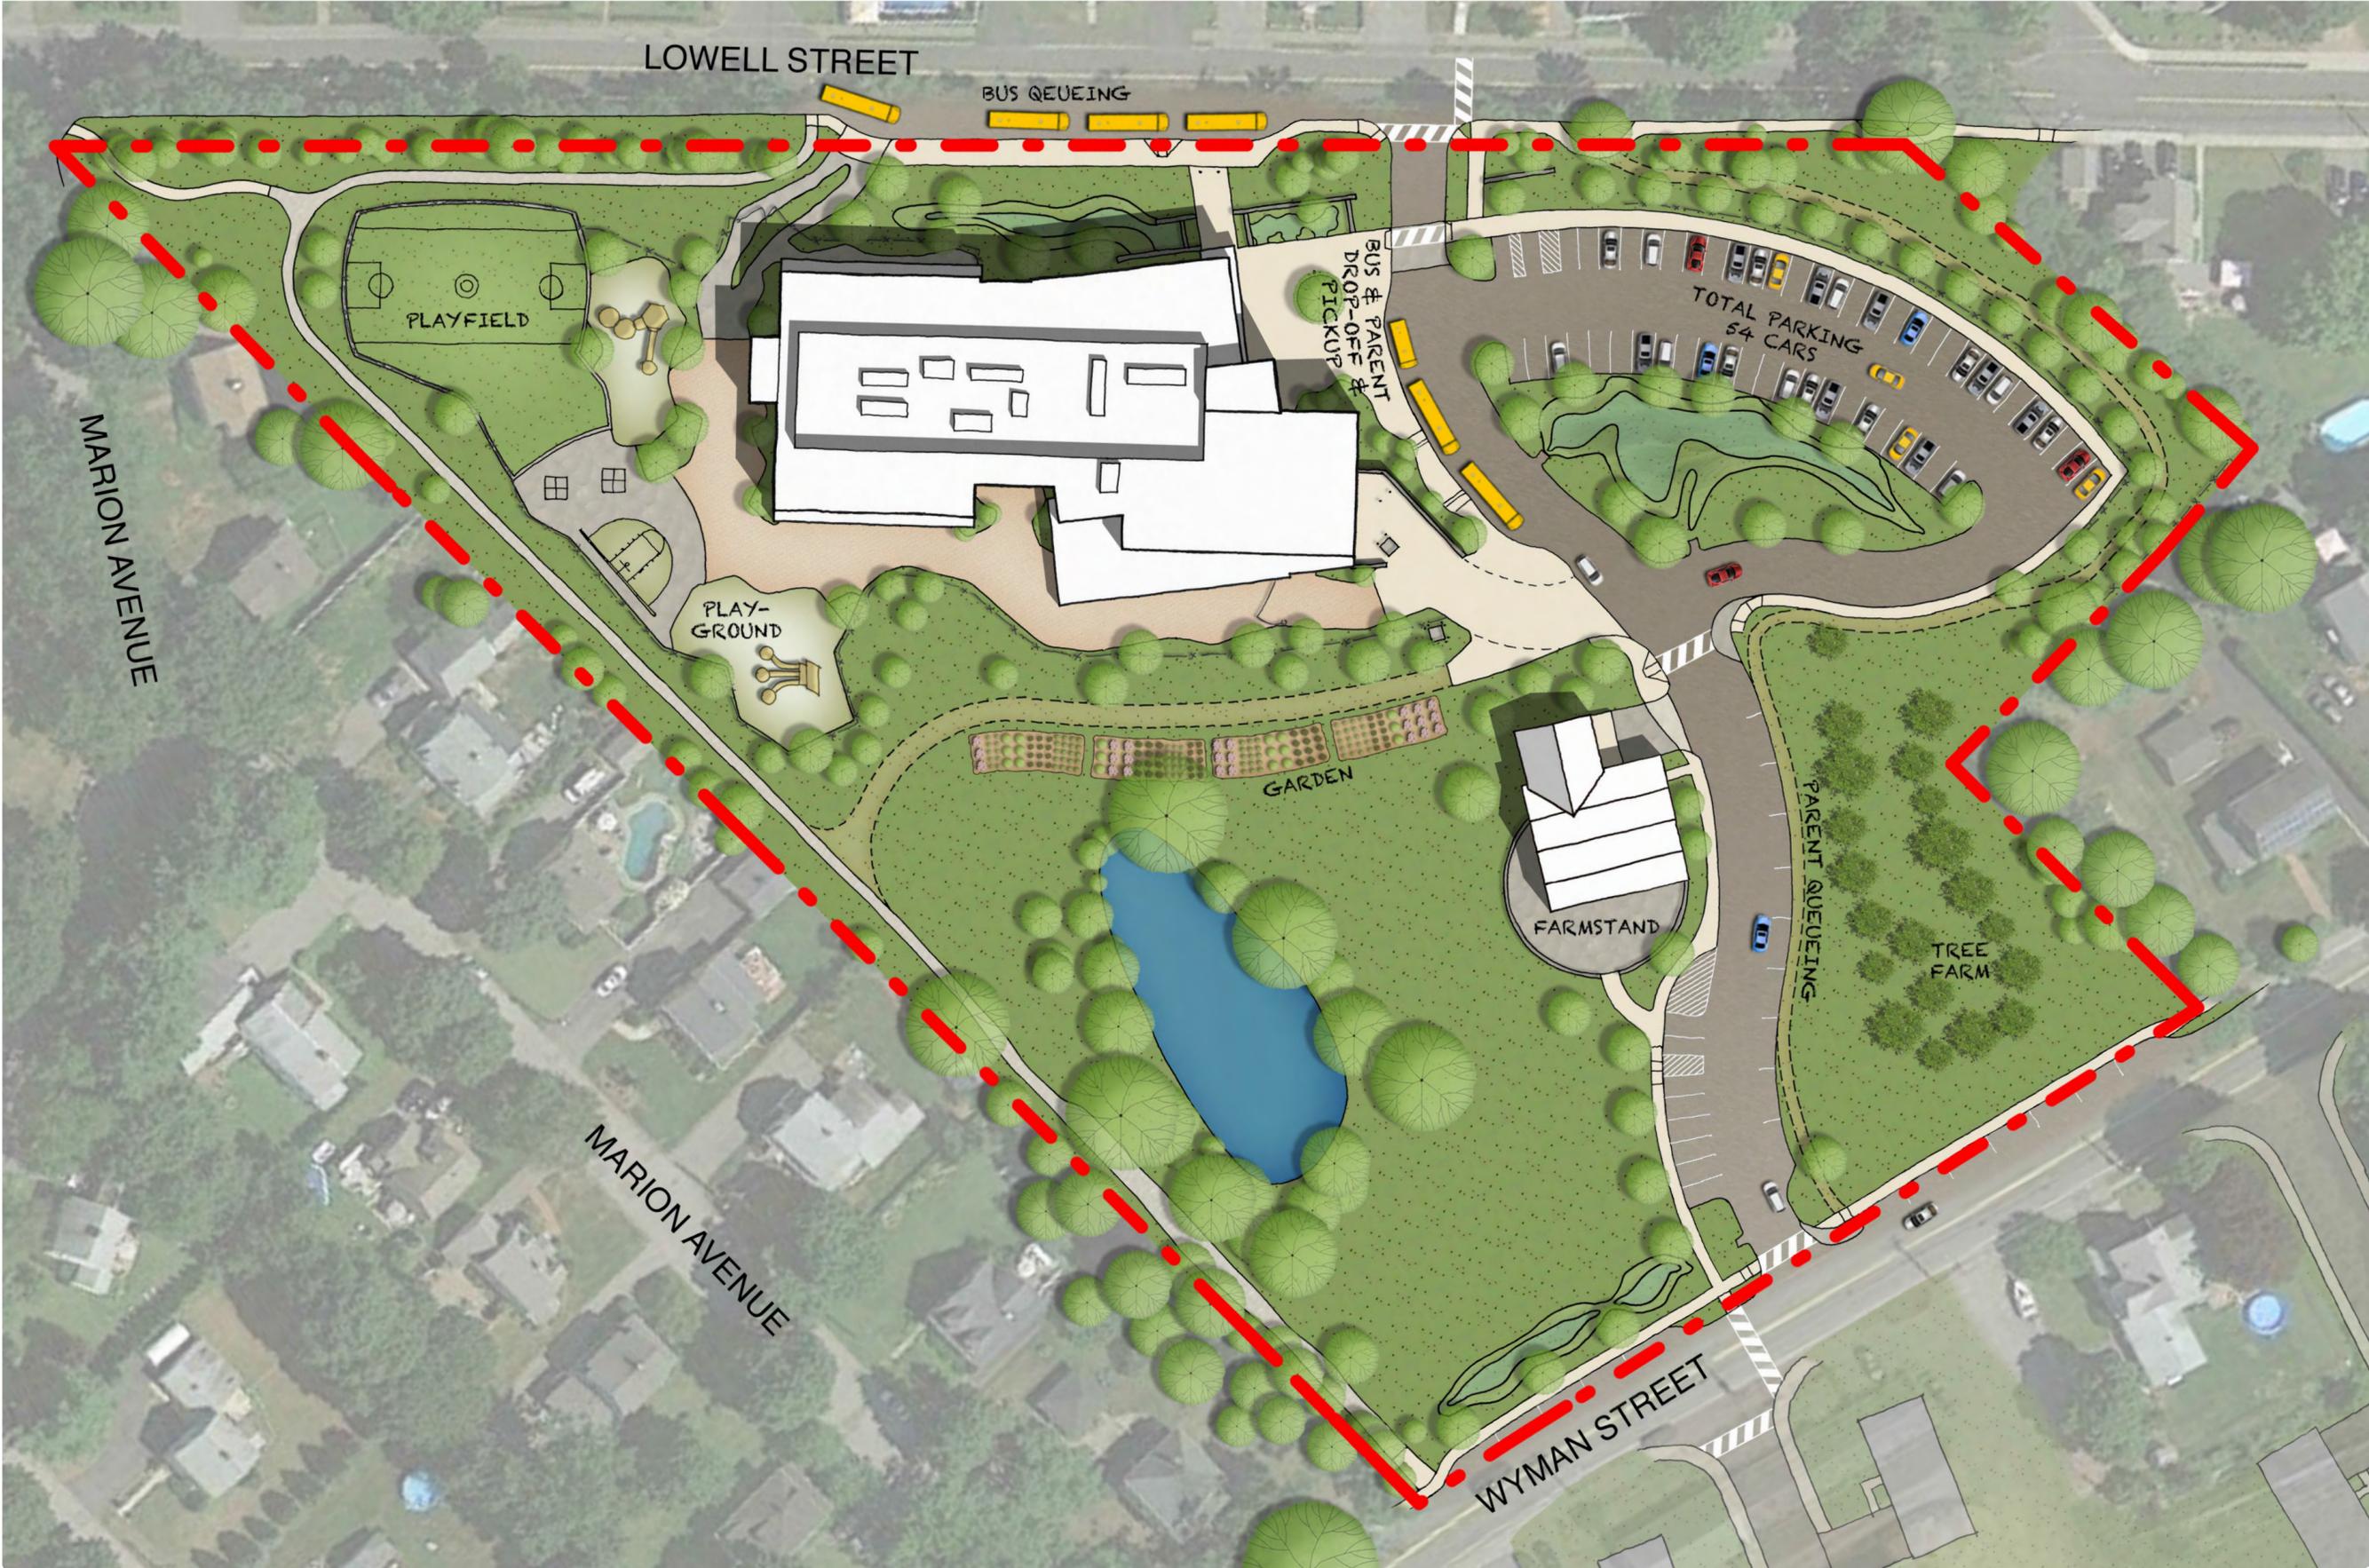

Perspective View




Perspective View



Design Studies | East Stair and Plaza




Construction Vehicle Route

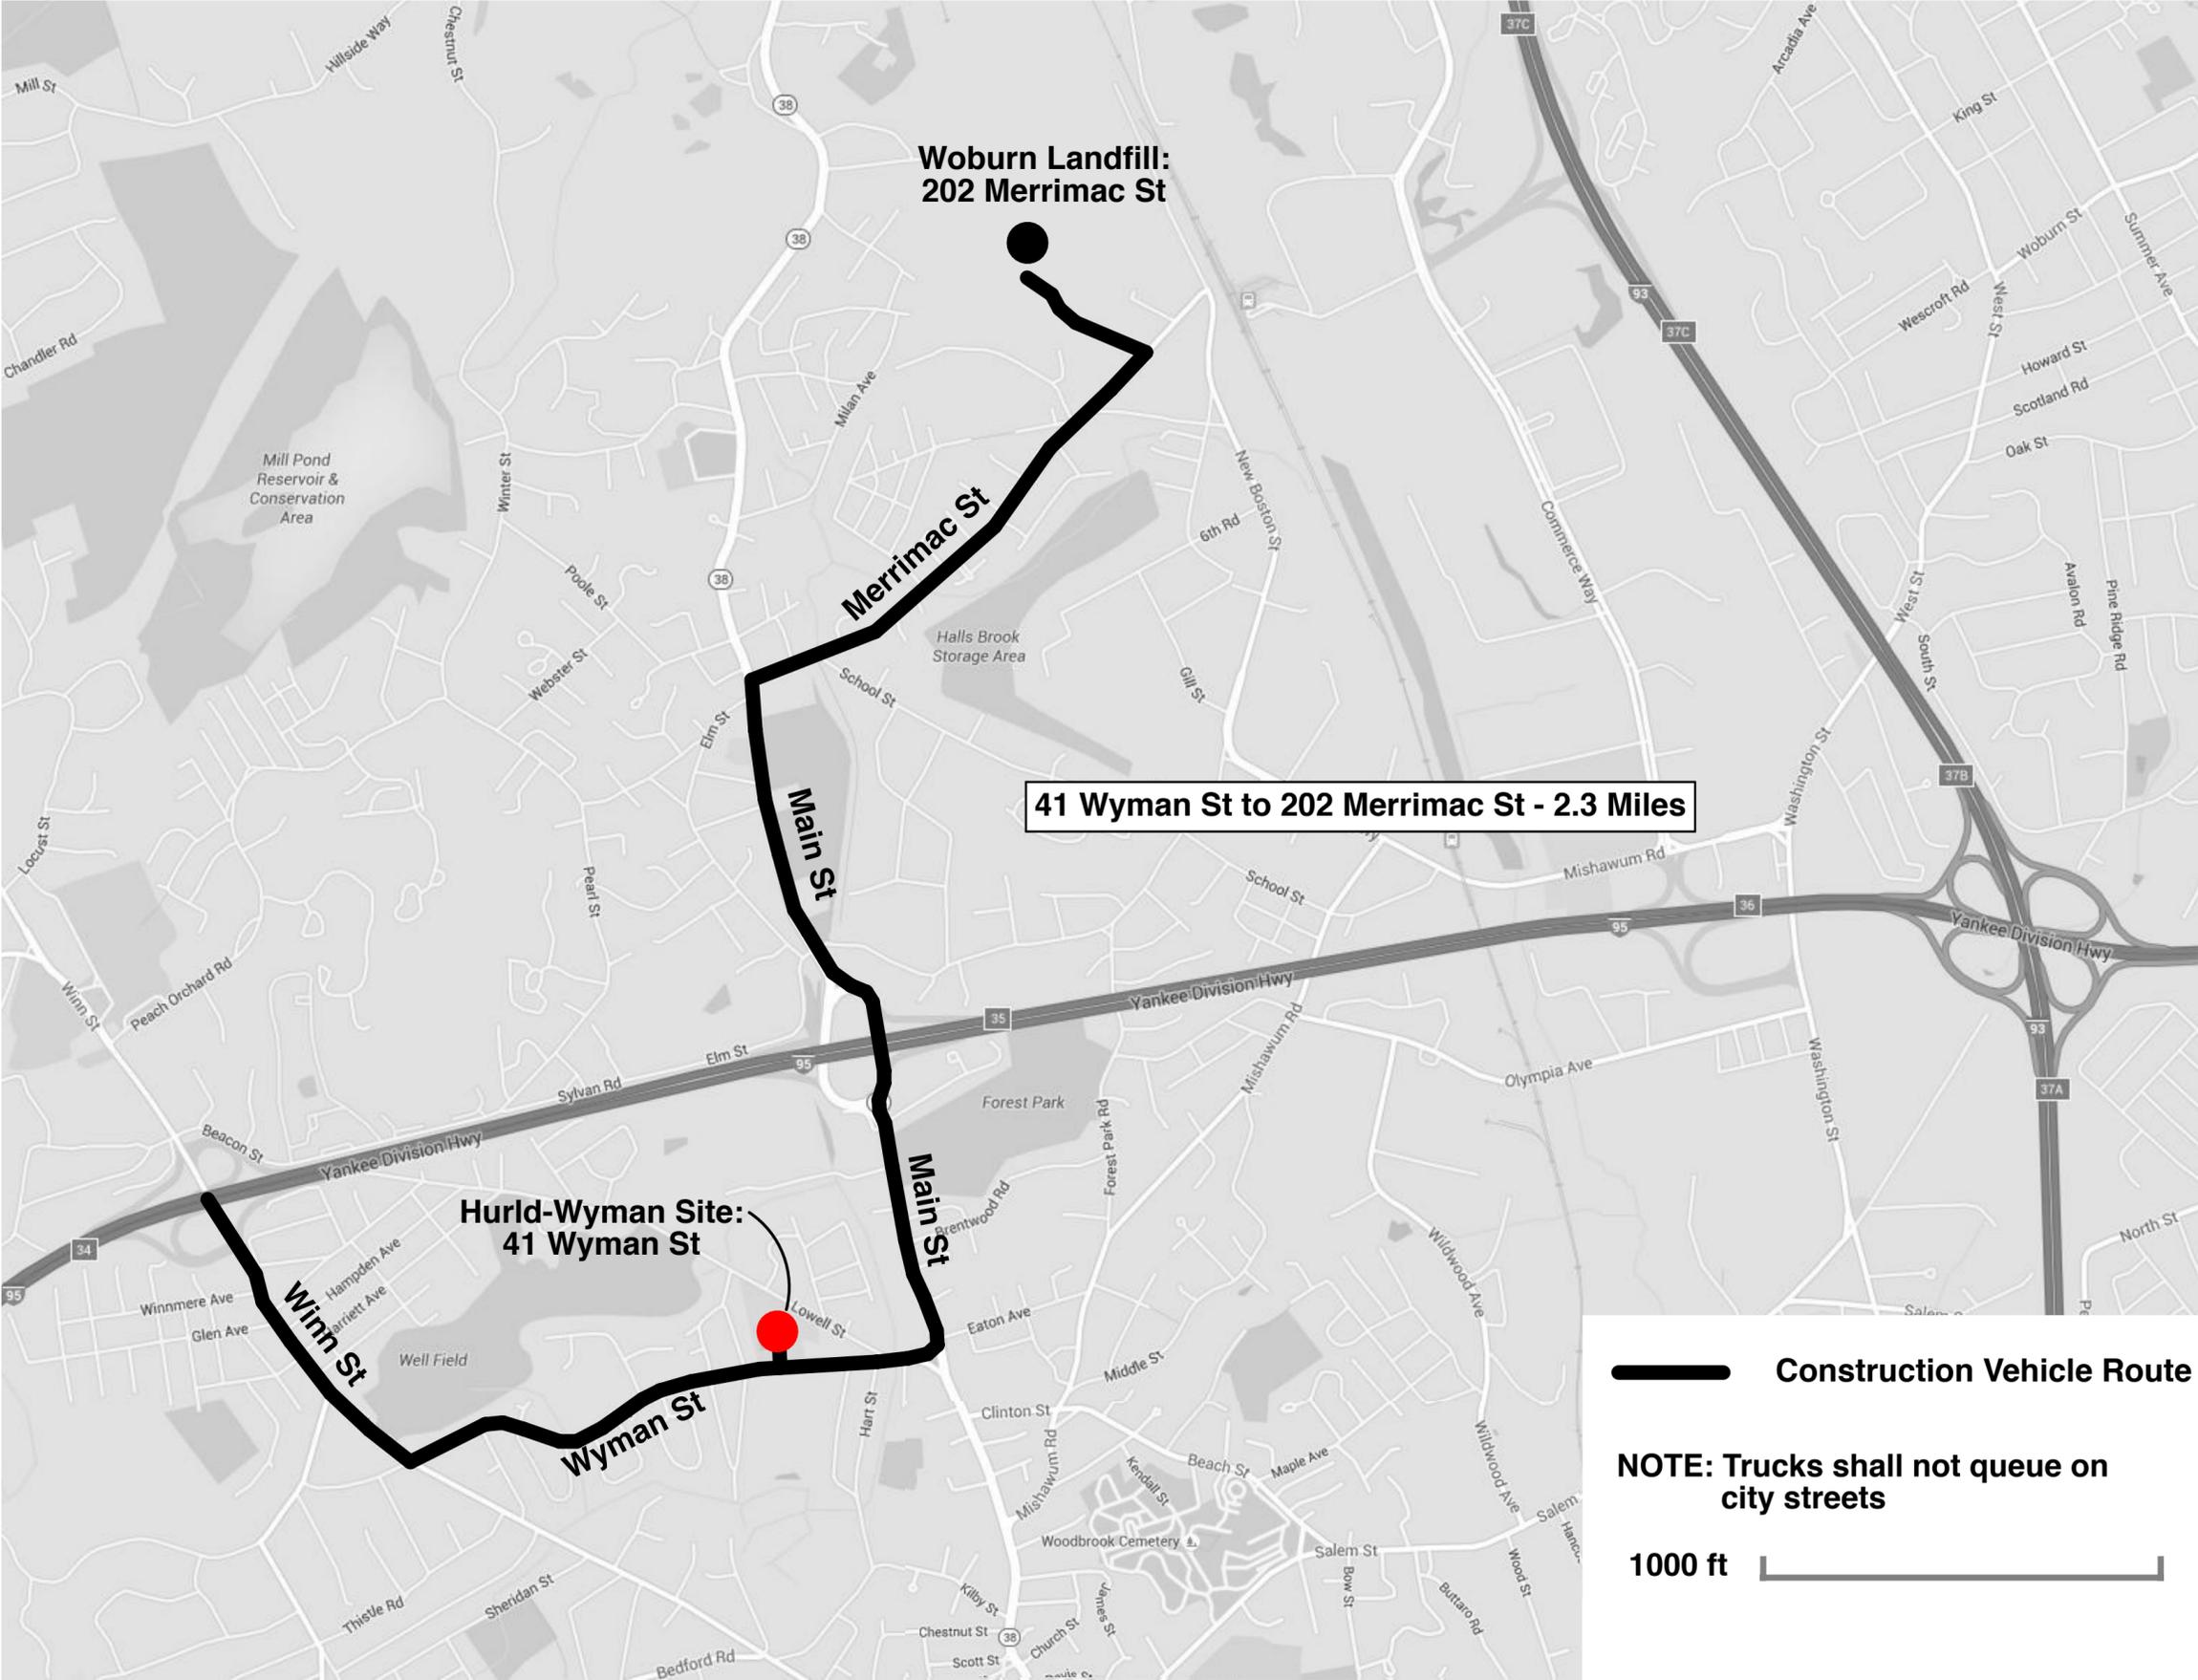

Construction Vehicle Route



Early Site Preparation - Limit Of Work

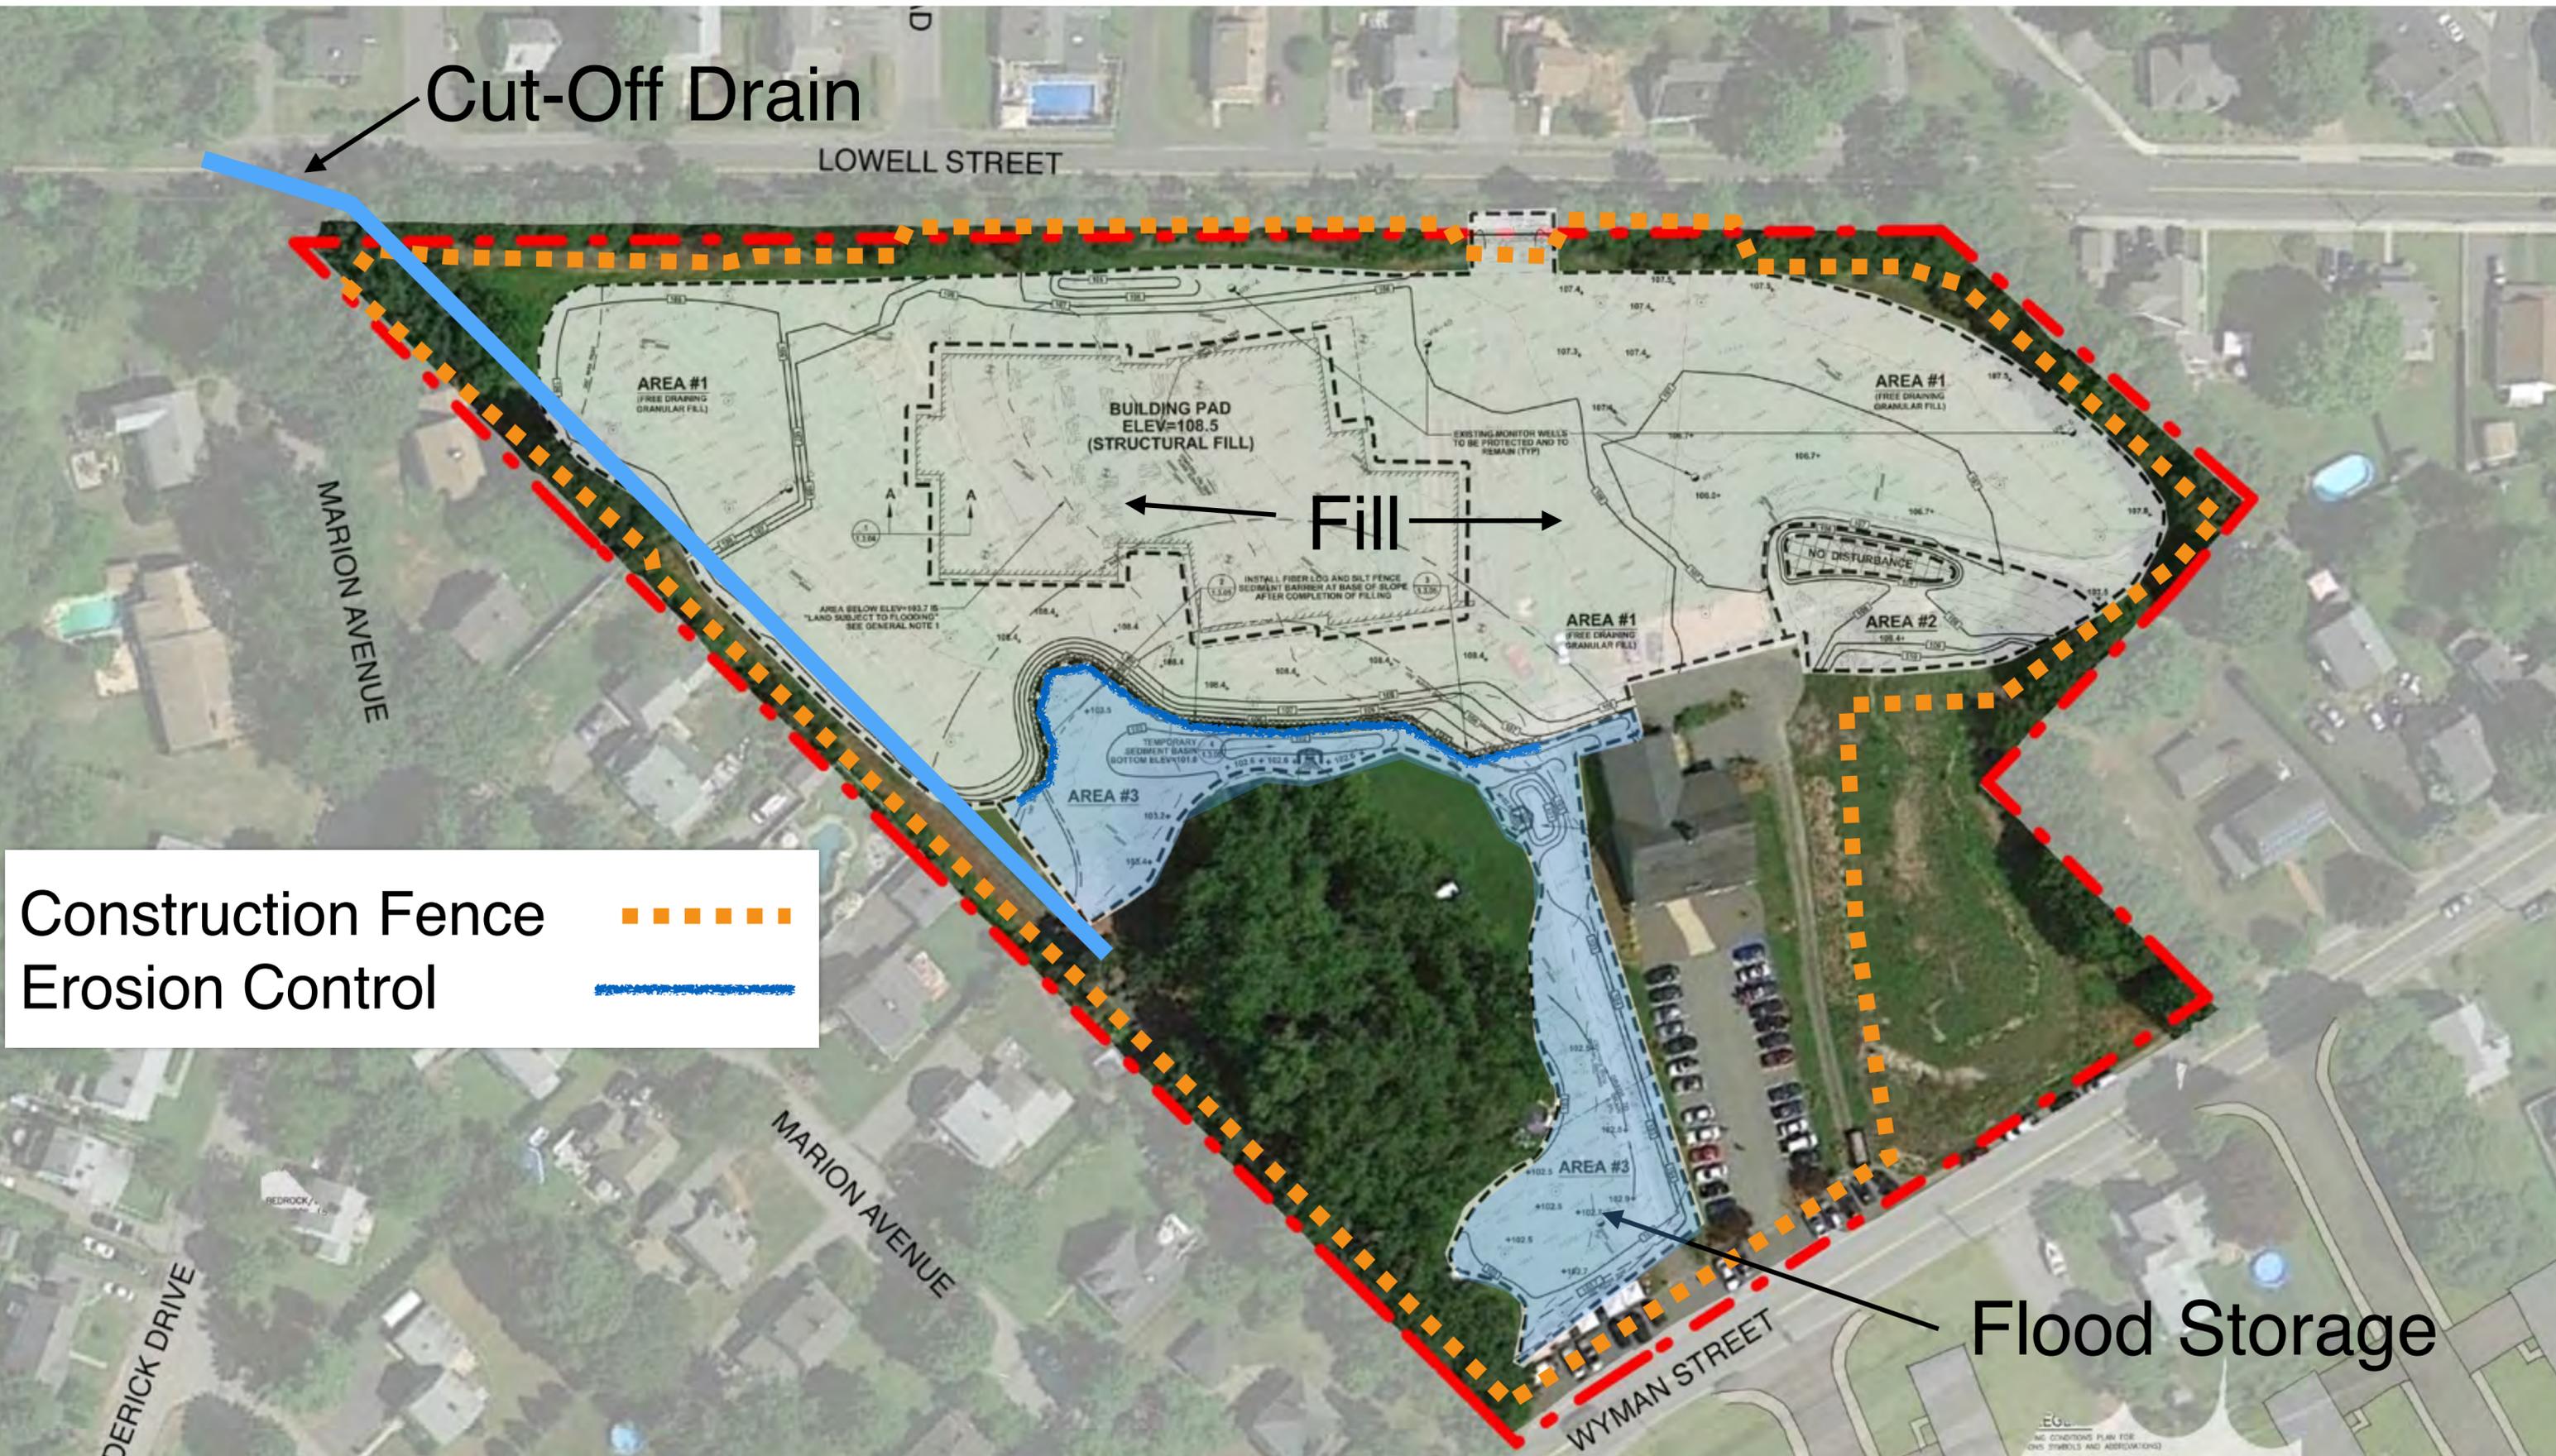

Construction Fence
Erosion Control




Flood Storage

Anticipated Construction Schedule

ID	Task Name	Duration	Start	Finish	2017				2018	
					Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2
1	Site Preparation / Utility Work	60 days	Mon 2/6/17	Fri 4/28/17						
2	Foundation Installation	30 days	Tue 2/21/17	Mon 4/3/17						
3	Structural Framing	60 days	Mon 4/17/17	Fri 7/7/17						
4	Exterior Envelope	100 days	Mon 6/26/17	Fri 11/10/17						
5	Building Interior	180 days	Mon 6/26/17	Fri 3/2/18						
6	Mechanical Systems	149 days	Tue 9/5/17	Fri 3/30/18						
7	Exterior Improvements - Phase 1	60 days	Fri 9/1/17	Thu 11/23/17						
8	Exterior Improvements - Phase 2	90 days	Mon 2/26/18	Fri 6/29/18						
9	Inspections / Close-out	60 days	Mon 4/9/18	Fri 6/29/18						
10	Anticipated Completion Date	1 day	Sat 6/30/18	Sat 6/30/18						


Building Progression / Phasing

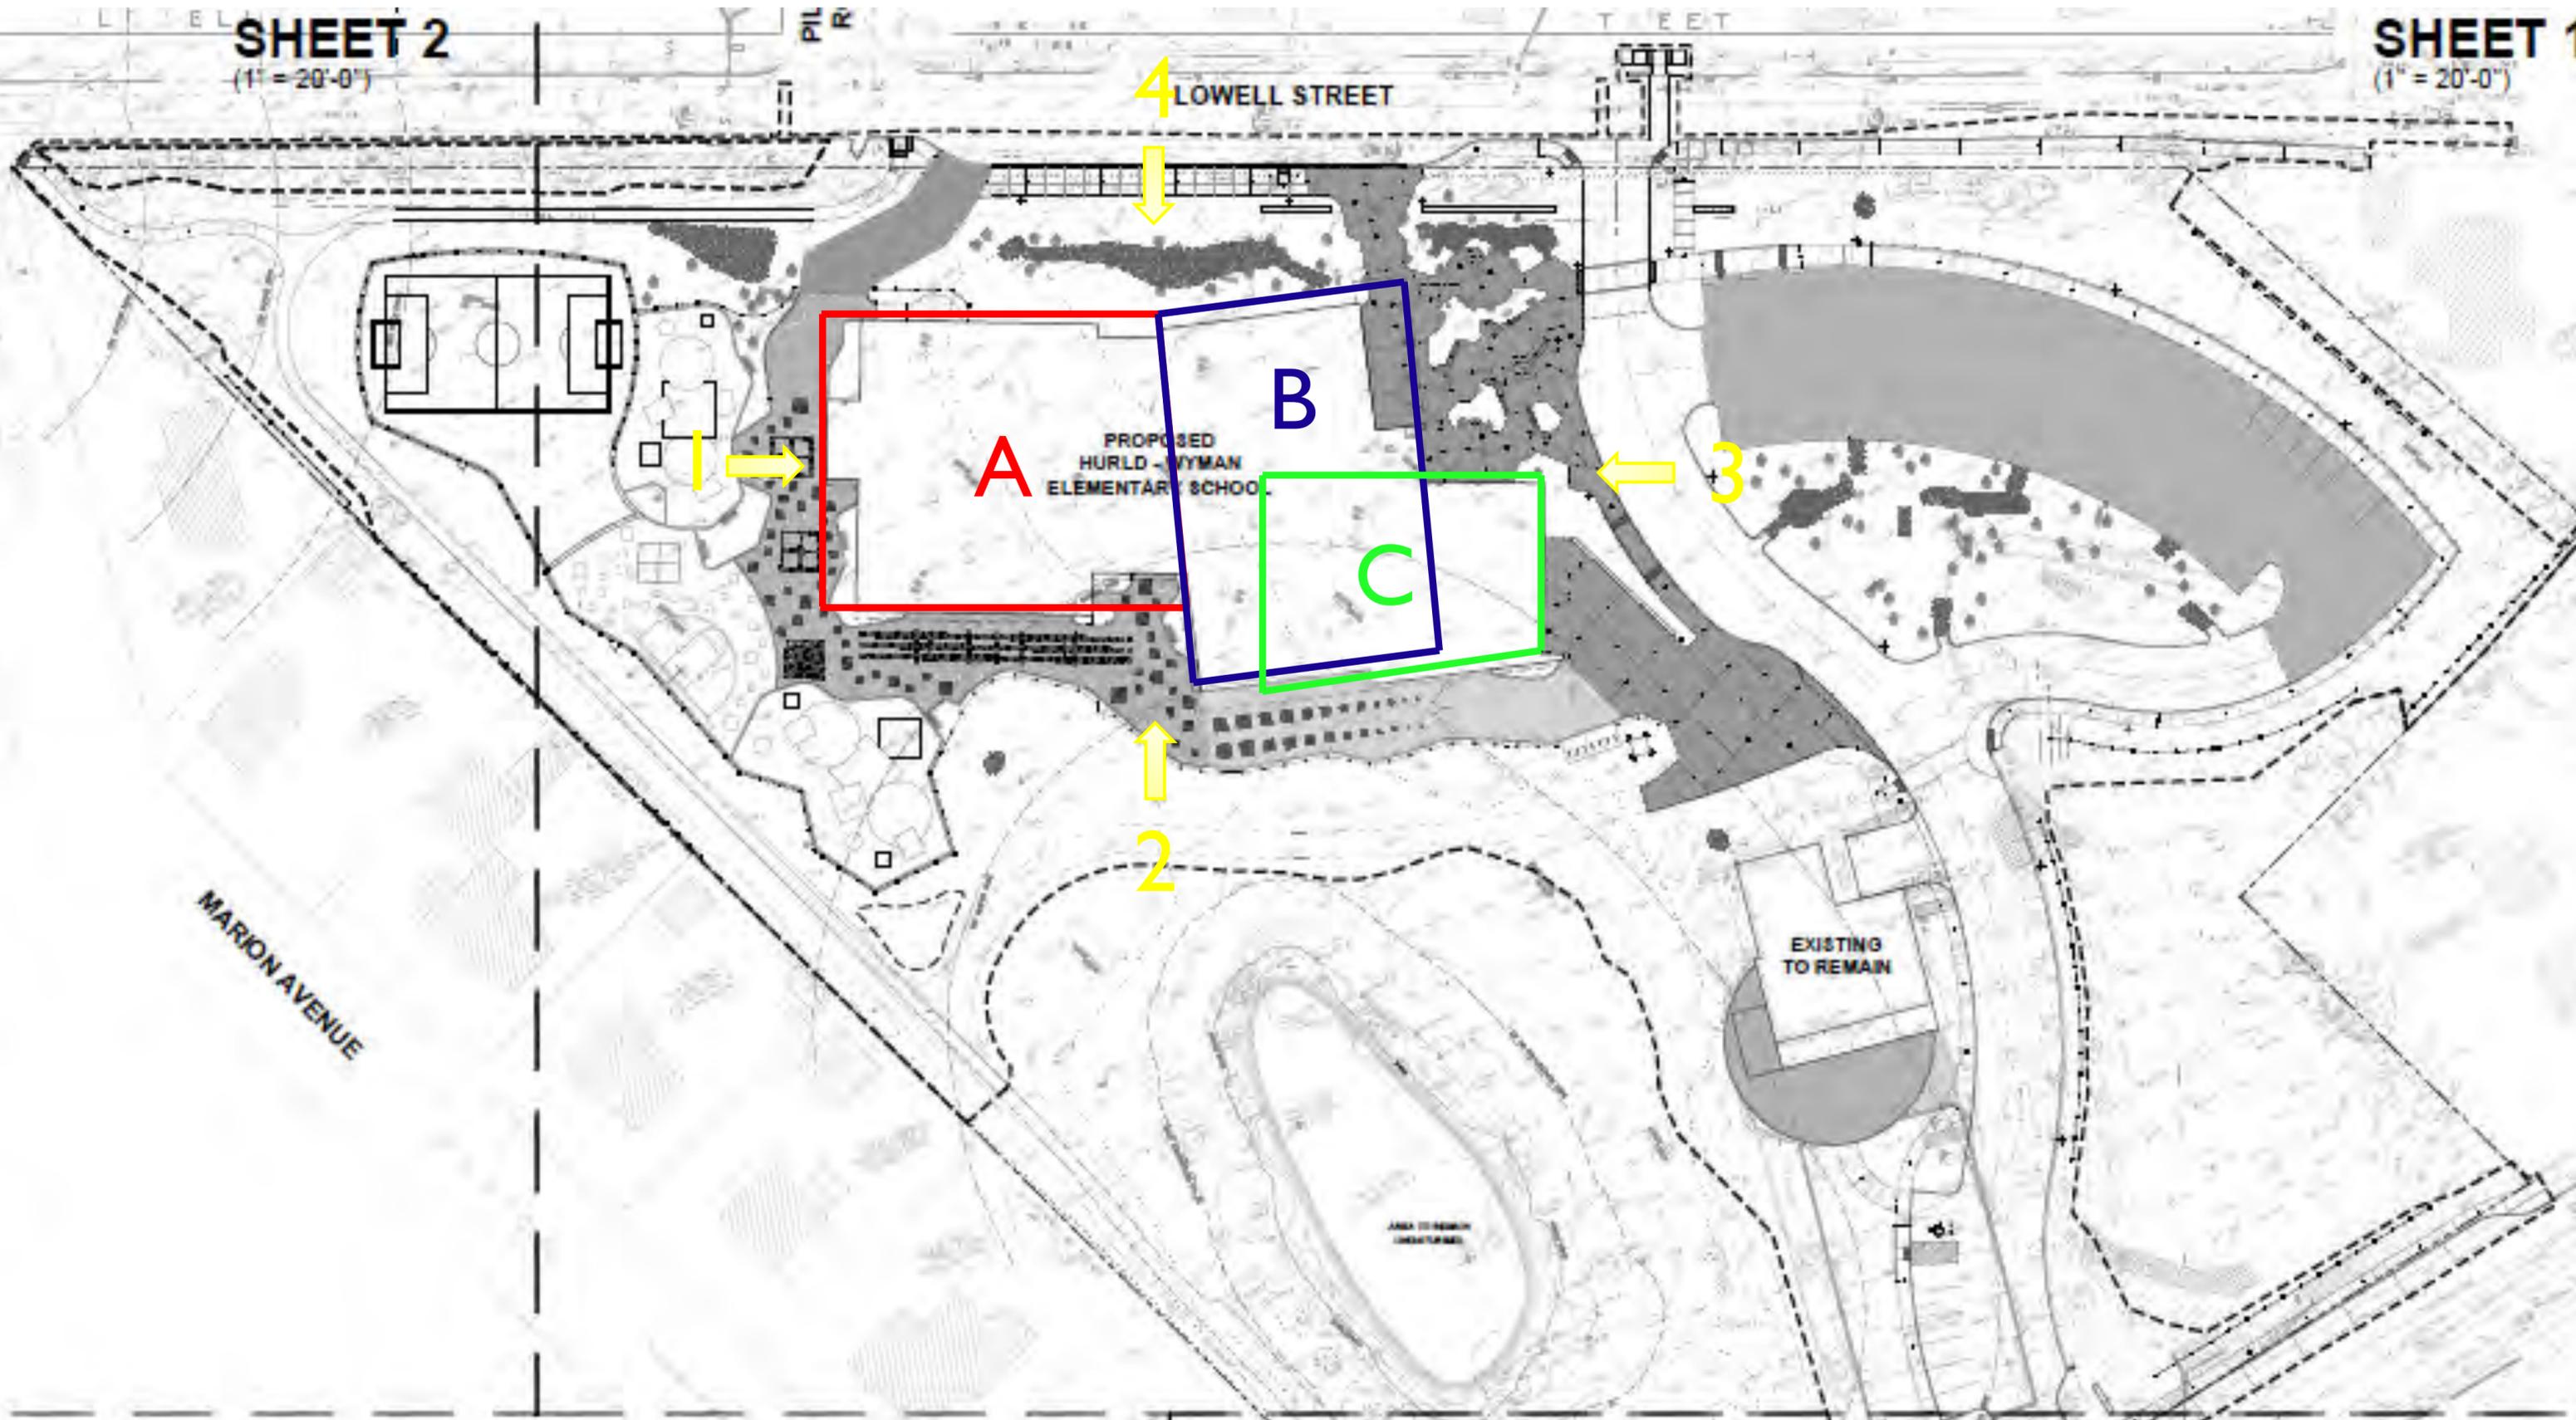


Potential Blasting Scope and 350' Radius

350' Survey Radius

Estimated Limit of Blasting Activity

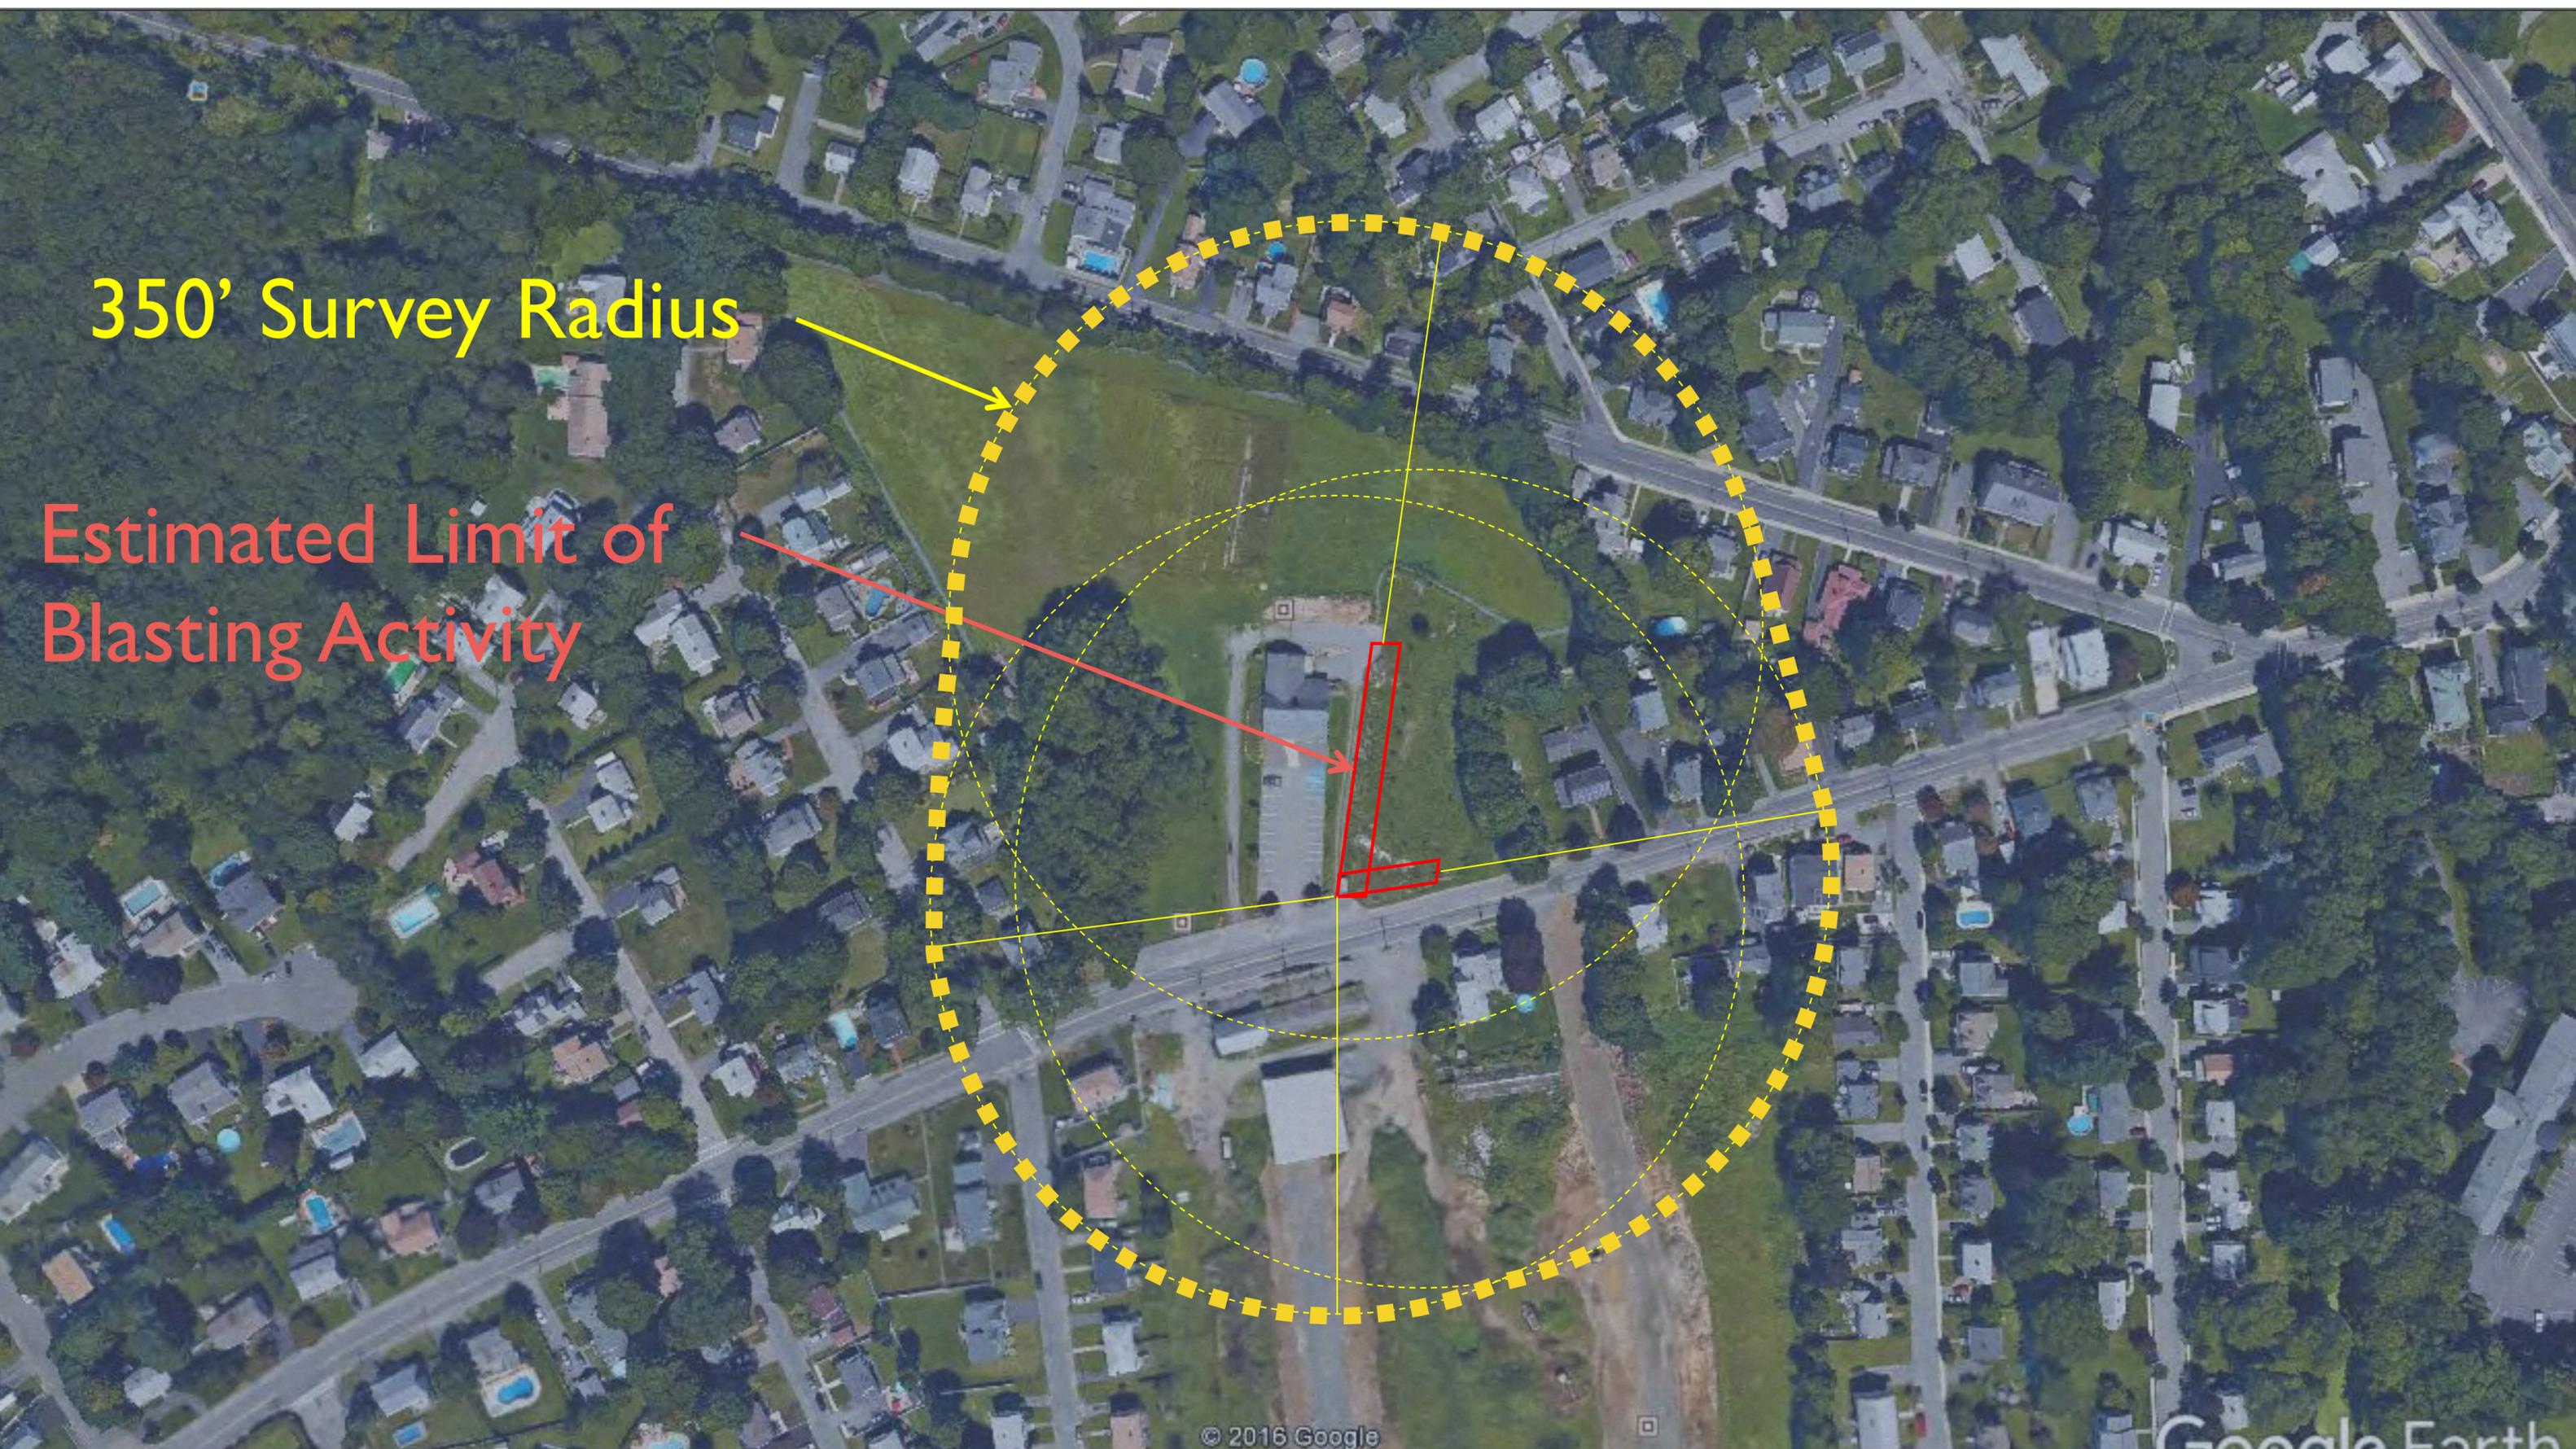

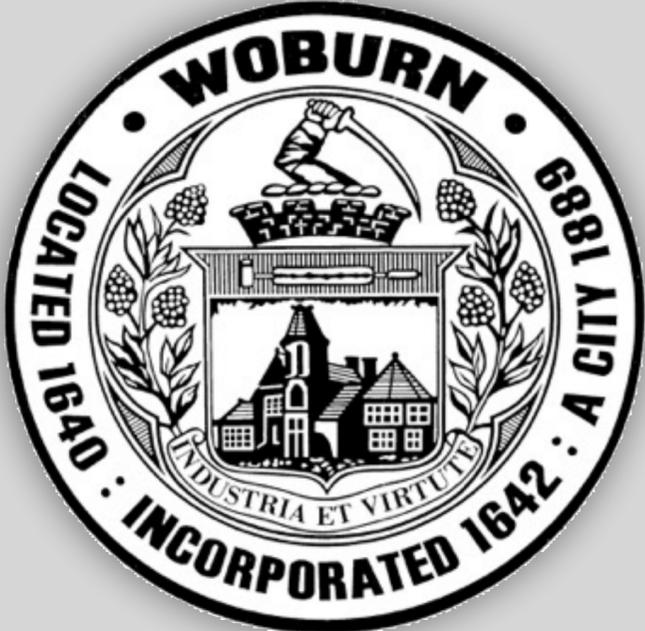

Hurd-Wyman Elementary School | Woburn

Neighborhood Meeting - March 01, 2017
